



Orange Business

NEW HIRE HANDBOOK

DPM Onboarding Handbook

Everything a new Delivery Project Manager needs to understand the role, the team, the tools, and how we deliver — in one place.

Contents

1	Welcome	3
2	What is a Delivery Project Manager?	4
3	The Team & Organisation	6
4	The Squads	8
5	Tools & Systems	9
6	The LAN Delivery Process (full steps + Gantt)	10
7	The WAN Delivery Process (full steps + Gantt)	19
8	Networking Fundamentals (Quick Reference)	24
9	Vendor Hardware (Quick Reference)	25
10	Your First Few Weeks	26
11	Key Terms & Where to Get Help	27

SECTION 1

Welcome

Welcome to the Europe Delivery Project Management team at Orange Business. This handbook is your starting point.

You've joined the team responsible for turning customer orders into working network and IT infrastructure across Europe. Whether a customer is refreshing the Wi-Fi across dozens of sites, replacing core switches, or rolling out SD-WAN, a Delivery Project Manager (DPM) is the person who makes it happen on time and without surprises.

This document explains **who we are, what we do, the tools we use, and how a delivery runs from start to finish** — including the full step-by-step LAN and WAN processes with their project timelines. It is written for someone brand new to the team — no prior knowledge assumed. Read it once end-to-end, then keep it as a reference.

Tip — pair this with the Knowledge Base. This handbook gives you the big picture. The internal **Network Knowledge Base** website goes deeper on each topic with diagrams, CLI examples, vendor hardware, the full process flowcharts, the live team directory, and a searchable glossary. Use them together.

How to use this handbook

- **Sections 2–4** introduce the role, the people, and how the team is organised.
- **Section 5** is your tool reference — bookmark it.
- **Sections 6–7** walk through the LAN and WAN delivery processes step by step, each with a Gantt timeline.
- **Sections 8–9** are quick technical primers so the conversations make sense.
- **Sections 10–11** help you get going and know where to turn for help.

SECTION 2

What is a Delivery Project Manager?

A DPM owns a customer's network delivery from the moment an order is placed through to final handover.

You are the **single point of accountability** that turns a signed order into working infrastructure on the customer's site. You don't configure every device yourself — you orchestrate the specialists, keep the plan on track, manage risk, and communicate clearly so the customer always knows where things stand.

Your four core responsibilities

Own the delivery

Drive each project from kickoff to HOTO sign-off — plan the timeline, track milestones, and keep order records accurate in GOLD, ServiceNow and SALTO.

Coordinate the teams

Orchestrate everyone the delivery depends on: TIMs and engineering, Field Engineers booked through FLIP, logistics, and the customer's own technical contacts.

Manage scope & risk

Confirm prerequisites, flag blockers early, run staging and dry runs, and document decisions so nothing is lost or disputed later.

Run the migration

Execute LAN/WAN cutovers — switches, WLCs and access points — support UAT with the customer, then close out every system once the site is live.

What good looks like

- The customer is never surprised — they always know the plan, the date, and the status.
- Prerequisites are confirmed *before* the migration window, not discovered during it.
- Every migrated service is tested and signed off, and every system is closed cleanly at the end.
- Issues are put on record factually and escalated early, while there is still time to act.

Who does what — the RACI matrix

Delivery is a team sport, but ownership must be unambiguous. This matrix shows who is **Accountable** and **Responsible** for each activity in a typical delivery — and where you consult or simply inform.

R Responsible — does the work **A** Accountable — owns the outcome (one per activity) **C** Consulted **I** Informed

Roles: PM = Project Manager (scope & commercial owner) · SC = Solution Consultant (design owner) · VPO / TIM = engineering & staging · FE = Field Engineer · Supply Chain = hardware logistics.

ACTIVITY	DPM	PM	SC	VPO / TIM	FE	SUPPLY CHAIN	CUSTOMER
Scope, BOM & commercial coordination	C	A R	C	—	—	—	C
GOLD / SALTO order creation & accuracy	A R	C	—	—	—	—	—
Hardware ordering, EDD & shipping	A	I	—	—	—	R	I
Runbook & LLD preparation	C	—	A R	C	—	—	C
Staging & migration date selection	A R	I	—	C	—	—	C
MACHX raises (VPO work orders)	A R	—	—	I	—	—	—
Field Engineer booking (FLIP)	A R	—	—	—	I	—	—
Change request (ServiceNow)	A R	I	—	C	—	—	I
Staging execution	A	—	C	R	—	—	C
Dry run	A	—	C	R	—	—	C
Migration / cutover execution	A	I	C	R	R	—	C
User Acceptance Testing (UAT)	A	—	—	C	—	—	R
Success notification & status comms	A R	I	—	—	—	—	I
DNAC / CMDB updates	A R	—	—	C	—	—	—
HOTO package & sign-off	A R	I	C	C	—	—	I
GOLD / SALTO order closure	A R	I	—	—	—	—	—

The DPM golden rule. The DPM is accountable for the delivery end-to-end — the **dates**, the **MACHX raises**, the **Field Engineer dispatch**, and the **HOTO package** are yours. The PM owns **scope, BOM and the commercial relationship**. Keeping these boundaries clear is what keeps a delivery calm.

Acronym you'll hear daily — HOTO. "Hand-Over-To-Operations": the formal sign-off at the end of a project where the delivered, tested environment is handed to the support/operations teams. Reaching a clean HOTO is the goal of every delivery.

SECTION 3

The Team & Organisation

The Europe DPM organisation sits within Order to Bill and is split into regional clusters, each led by a manager.

The clusters

Each manager leads a cluster of DPMs. Within a cluster, the DPMs are peers — they pick up deliveries across the cluster's territory.

MANAGER	CLUSTER	TERRITORY FOCUS
Karim El Zarka	N&S EU (Inc. Trans)	North & South Europe transversal delivery
Mona Tantawy	Swiss	DACH / Switzerland territory
Peter Sabet	GEA	Southern Europe transversal delivery
Maryam Etry	Benelux	Belgium, Netherlands, Luxembourg


Subject Matter Experts (SMEs)

Some DPMs also act as **Subject Matter Experts** — go-to people for deeper technical or process questions. Current SMEs include **Abanoub Wasfy** and **Salma El Shazly** (N&S EU), **Ahmed Hweedy** (Benelux) and **Emad Osman** (GEA). They appear with a **DPM / SME** tag on the cluster pages.

The live directory is on the website. Every cluster has its own page on the Knowledge Base listing all DPMs with their name, email and cluster. The list is kept up to date there — so this handbook intentionally names managers and SMEs only, and points you to the site for the full, current team.

The Management Chart

Europe Delivery Project Management, Order to Bill — managers by cluster, with Subject Matter Experts shown under their manager.

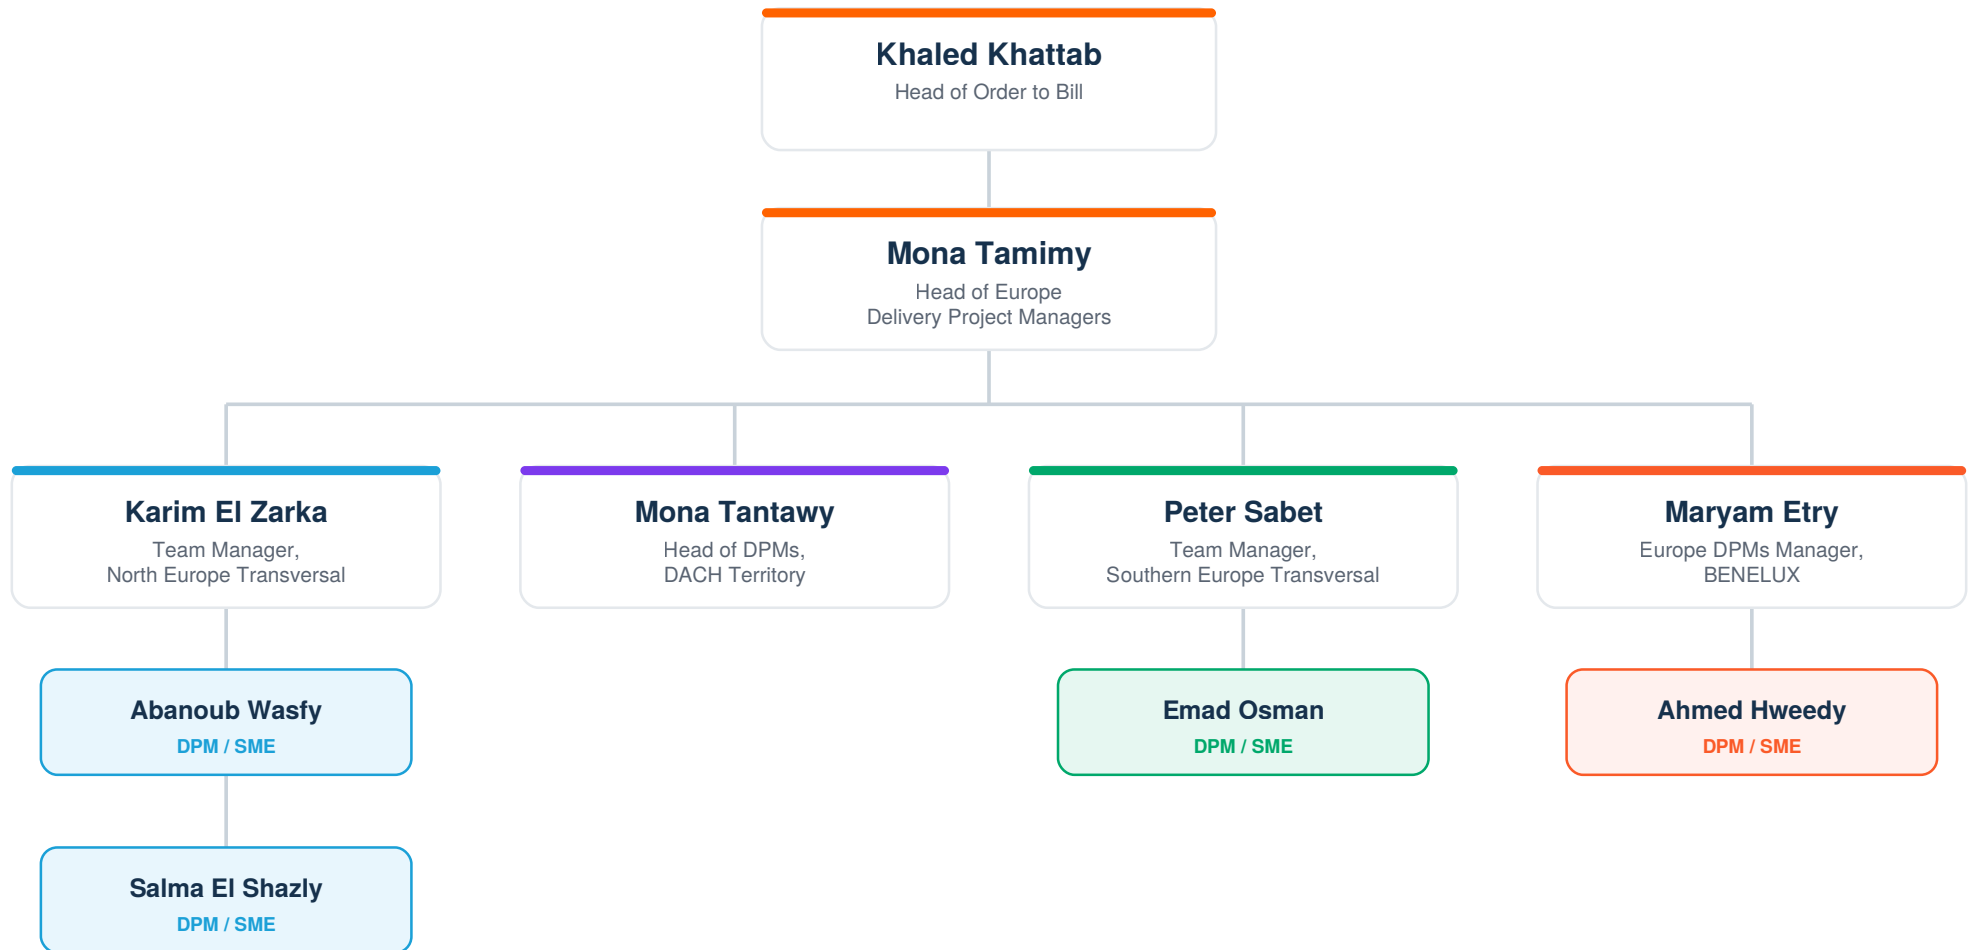

SECTION 4

The Squads

Alongside delivery work, DPMs join cross-team "squads" — small working groups that keep the function running and improving.

Squads are how we share the load on things that benefit the whole team rather than a single customer. Joining one is a great way to make an impact early and get to know people across clusters.

SQUAD	WHAT IT DOES
Automation	Builds the automations and dashboards that save the team manual effort and give visibility into delivery.
Marketing	Internal marketing and communications for the DPM function — telling the story of what we deliver.
Hiring	CV screening and interviews — helping grow the team with the right people.
Onboarding	Welcomes and ramps up new joiners (this handbook is part of that effort).
Pre-Sales	Solution input, scoping and bid support — helping shape deals before they become deliveries.

Members change over time. Each squad has its own page on the Knowledge Base with the current members and their contact details. Ask your manager which squad is the best fit for your strengths and interests.

SECTION 5

Tools & Systems

These are the systems you'll use most. You don't need to master them on day one — learn them as they come up in your first deliveries.

Core delivery tools

TOOL	WHAT YOU USE IT FOR
GOLD	Order management. Where the customer order lives; you track and ultimately close the GOLD order at the end of delivery.
ServiceNow (SNOW)	Raising change requests and updating the CMDB (the record of what's installed). Used for change control around migration windows.
MACHX	Raising and managing TIM / VPO work orders — the requests that get engineering/staging work done. An AP job needs one raise; a Switch/WLC job needs two.
FLIP	Booking Field Engineers to attend site. Used on Switch/WLC deliveries where hardware is handled on-site.
DNAC / Catalyst Center	Cisco's network management platform. Post-migration, you send the DNAC update so the new devices are managed and monitored.
SALTO	A second order system that is closed post-migration alongside GOLD.
SharePoint	Where delivery documents live — you upload the HOTO document, runbook and LLD (Low-Level Design) for each project.

Reporting, time & automation

TOOL	WHAT YOU USE IT FOR
Oracle PRIME	Time entry — logging hours against projects.
Power BI	Dashboards and reporting on delivery status and KPIs.
Power Automate / Office Scripts	Automating repetitive steps (reminders, data prep) — much of it built by the Automation squad.

Quick mental model. **GOLD/SALTO** = the order. **ServiceNow/MACHX** = getting the work approved and done. **FLIP** = people on site. **DNAC** = managing the result. **SharePoint** = the paperwork. **PRIME/Power BI** = your time and the reporting.

SECTION 6

The LAN Delivery Process

Every delivery follows the same three phases. LAN delivery comes in two flavours — the AP (wireless) process and the WLC & Switch process — each documented below with its full step list and an indicative Gantt timeline.

PHASE 1

Pre-migration

Confirm supply, raise MACHX, validate prerequisites, stage hardware, and run dry runs with the customer.

PHASE 2

Migration

Execute the cutover in the agreed window, support the field/VPO teams, and run UAT on every migrated service.

PHASE 3

Post-migration / HOTO

Send the success notification, update DNAC/CMDB, upload the HOTO pack, and close the GOLD and SALTO orders.


AP vs WLC/Switch — key differences

TOPIC	AP PROCESS	WLC / SWITCH PROCESS
Physical install	Customer mounts the APs	Field Engineer booked via FLIP
Staging	VPOs stage remotely	Formal staging session + post-staging email
Dry run	Internal — VPO & SC only	External — VPO, SC & customer; check 3rd-party servers
Unique pre-check	Option 43 must be verified	Second MACHX raise before migration
UAT	Test all SSIDs, then per-AP	Test all services on each migrated switch
MACHX raises	One	Two (pre-staging + pre-migration)

6.1 LAN — AP Process (full steps)

Source project plan: *MLAN Tasks (APs)*. The timeline below is indicative of a single-site delivery.

Project timeline — Gantt chart

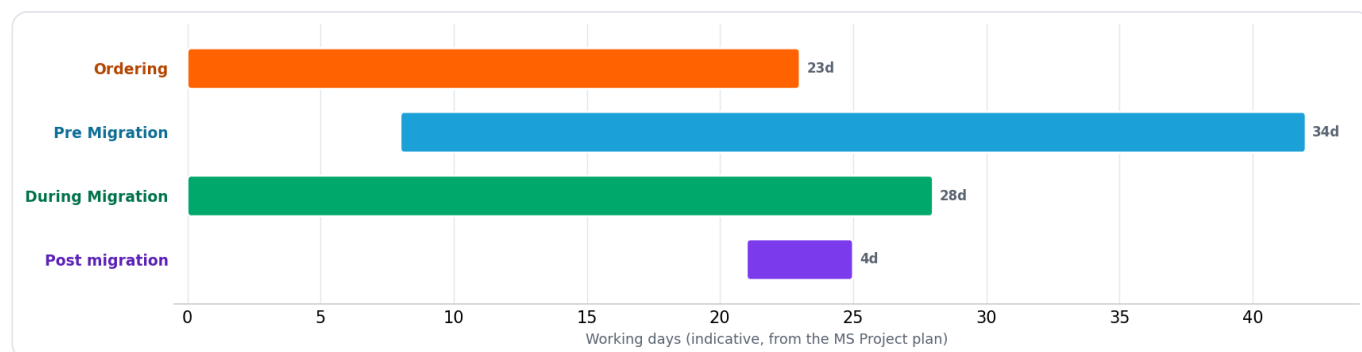

Colour-coded phase timeline for the LAN AP process. Each bar matches its step card below.

1 Ordering

23d · 2026-07-16 → 2026-08-17

- 1 Make sure GOLD Order is created with the right scope
- 2 Make sure SALTO order is created correctly with the GOLD Order scope
- 3 Assign GOLD order to yourself
- 4 Contact supply chain for ordering progress
- 5 Get an EDD (Estimate date of delivery)
- 6 Confirm devices have successfully arrived to the warehouse
- 7 Confirm with the consultant that the (runbook + LLD) are being prepared for the site
- 8 Check whether the devices to be staged in the warehouse or customer site
- 9 Stage devices are warehouse if needed (Send FE to site)
- 10 Raise Shipping alert for the devices to the customer site
- 11 Finish Phase 1

2 Pre Migration

34d · 2026-07-24 → 2026-09-09

- 1 Confirm with supply chain that order has arrived at customer site.
- 2 Send customer and confirm with them.
- 3 Confirm with SC that runbook is prepared
- 4 Set up a call with the customer to align on a possible migration date and explain that the customer will be the one mounting the APs.
- 5 Send customer to connect APs to switch
- 6 Send to the VPOs to stage the APs
- 7 Send customer the UAT Test document
- 8 Get confirmation from the customer on the migration date (By email)
- 9 Raise change request on SNOW (Service Now)
- 10 Check that Option 43 is configured.
- 11 Raise option 43 request if needed
- 12 Raise MACHX for the VPOs
- 13 Get the answered UAT document from the customer
- 14 Send migration invitations for the customer and VPO (PM and SC should be included as optional in all migrations)
- 15 Finish phase 2

3 During Migration

28d · 2026-07-16 → 2026-08-24

- 1 Join the migration call
- 2 Keeping track of all the APs that are migrated and pending to be migrated
- 3 Asking customer to do UAT for all SSIDs and then for all APs
- 4 Asking customer to fully test all services connected to the APs.
- 5 Get confirmation from customer that everything is working.
- 6 Finish Phase 3


4 Post migration

4d · 2026-08-06 → 2026-08-11

- 1 Send Success Notification
- 2 Send CMDB Update
- 3 Send DNAC Update
- 4 Close GOLD Order
- 5 Close Salto Order
- 6 Upload HOTO Document and Runbook (including LLD) on sharepoint
- 7 Send HOTO Document for the HOTO Manager

AP Process — the complete plan, task by task


The complete plan at a glance — every task in order, colour-coded by phase, with its duration from the MS Project plan. Diamonds are milestones.

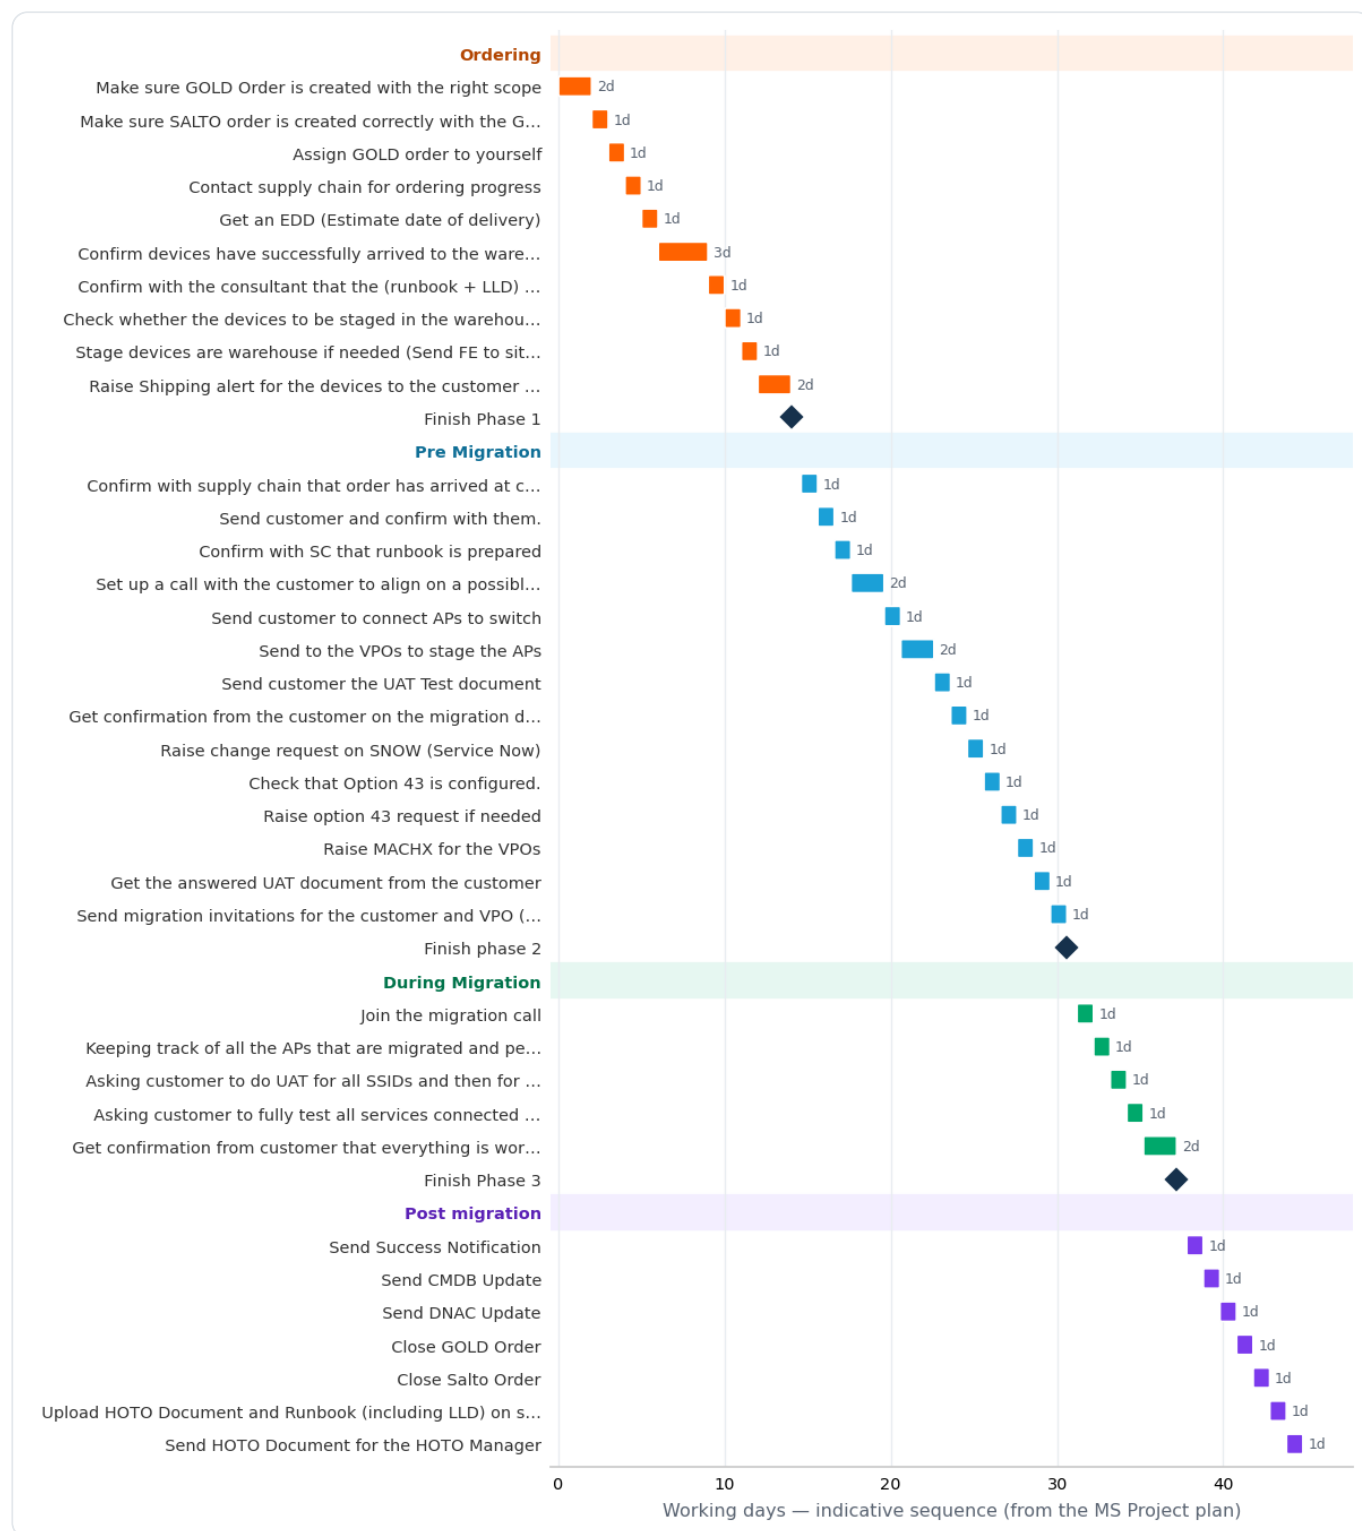

6.2 LAN — WLC & Switch Process (full steps)

Source project plan: *MLAN Tasks (WLC and Switches)*. The timeline below is indicative of a single-site delivery.

Project timeline — Gantt chart

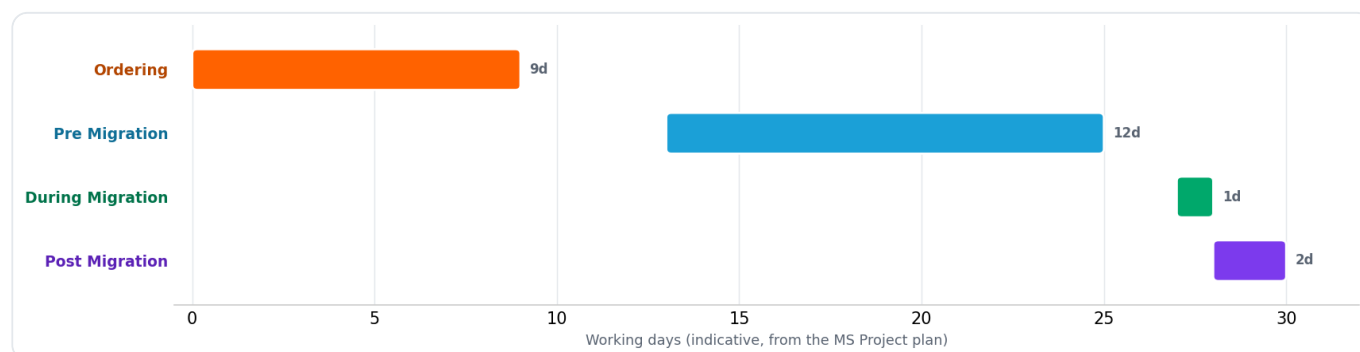

Colour-coded phase timeline for the LAN WLC & Switch process. Each bar matches its step card below.

1 Ordering 9d · 2026-07-15 → 2026-07-27

- 1 Make sure GOLD Order is created with the right scope
- 2 Make sure SALTO order is created correctly with the GOLD Order scope
- 3 Assign GOLD order to yourself
- 4 Contact supply chain for ordering progress
- 5 Get an EDD (Estimate date of delivery)
- 6 Confirm devices have successfully arrived to the warehouse
- 7 Confirm with the consultant that the (runbook + LLD) are being preapred for the site
- 8 Check whether the devices to be staged in the warehouse or customer site
- 9 Stage devices are warehouse if needed (Send FE to site)
- 10 Raise Shipping alert for the devices to the customer site
- 11 Finish Phase 1

2 Pre Migration

12d · 2026-07-28 → 2026-08-12

- 1 Confirm with supply chain that order has arrived at customer site.
- 2 Send customer and confirm with them.
- 3 Get IP addresses from the TDT
- 4 Confirm with SC that runbook is prepared
- 5 Set up external dry run with VPO and SC, and customer
- 6 Set up dates for the staging with the customer
- 7 Book Field Engineer
- 8 Raise MACHX for the VPOs
- 9 Send invitation for Staging
- 10 Staging Activity
- 11 Send post staging email, including daily status (in case than more one day)
- 12 Follow up external dry run with VPO, SC, and customer (Check for 3rd Party Servers).
- 13 Send customer the UAT Test document
- 14 Get confirmation from the customer on the migration date
- 15 Raise change request on SNOW (Service Now)
- 16 Align any teams you will need during migration (DXC, ODC, DHCP) Team
- 17 Raise MACHX for the VPOs
- 18 Get the answered UAT document from the customer
- 19 Send migration invitations for the customer and VPO (PM and SC should be included as optional in all migrations)
- 20 Finish phase 2

3 During Migration

1d · 2026-08-11 → 2026-08-11

- 1 Join the migration call
- 2 Keeping track of all the switches that has been migrated and which are still pending
- 3 Asking customer to fully test all services connected to the migrated switches
- 4 Get confirmation from customer that everything is working.
- 5 Finish phase 3


4 Post Migration

2d · 2026-08-12 → 2026-08-13

- 1 In case of multiple migration days send partial migration email (template provided); in case one day, or last migration day, send success notification
- 2 Send CMDB Update
- 3 Send DNAC Update
- 4 Close GOLD Order
- 5 Close Salto Order
- 6 Upload HOTO Document and Runbook (including LLD) on sharepoint
- 7 Send HOTO Document for the HOTO Manager
- 8 Finish phase 4

WLC & Switch Process — the complete plan, task by task

The complete plan at a glance — every task in order, colour-coded by phase, with its duration from the MS Project plan. Diamonds are milestones.

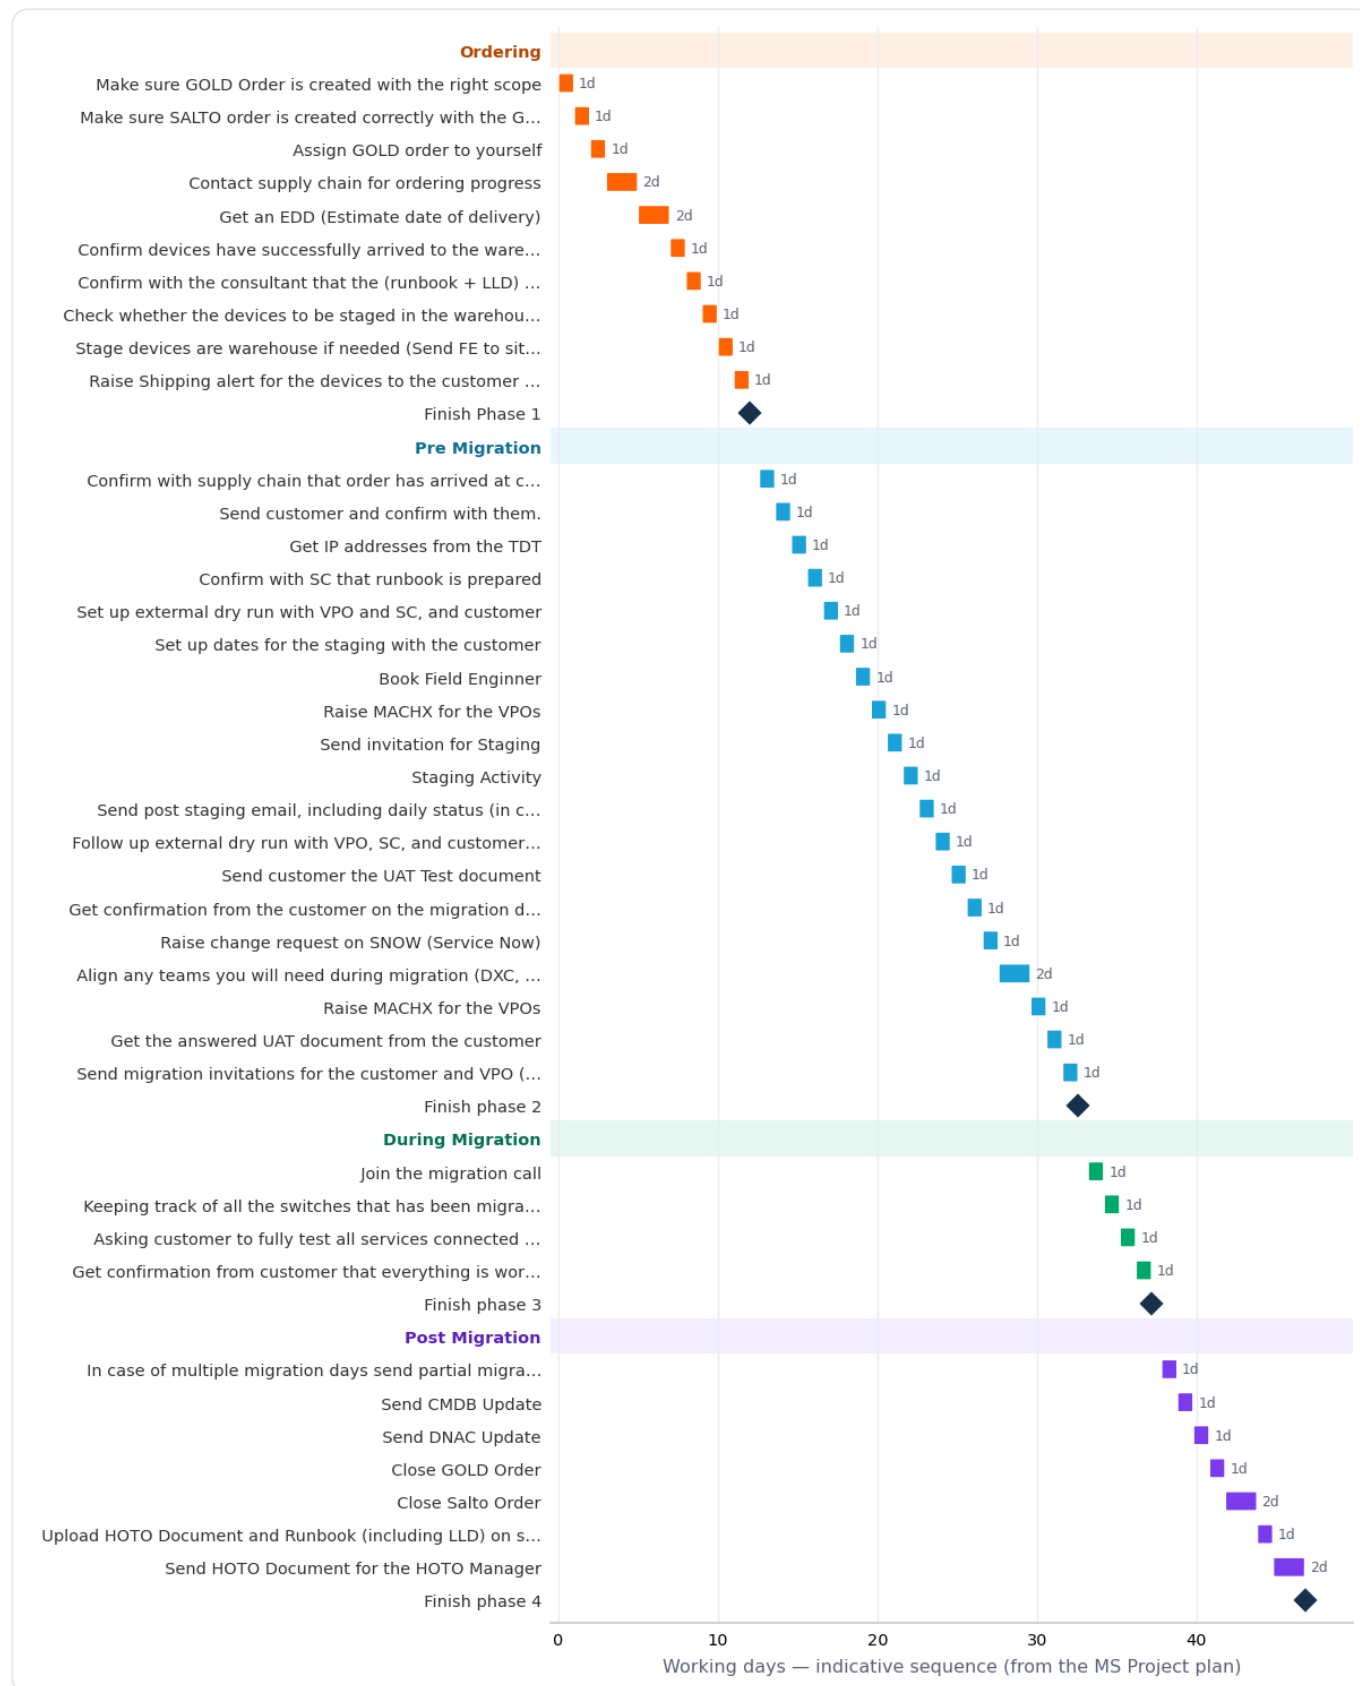

On the website. The Knowledge Base "LAN Process" pages present these same steps as interactive phase-by-phase flowcharts, with the exact tools and teams involved at each step. Use them as your live checklist on a delivery.

SECTION 7


The WAN Delivery Process

WAN delivery (SD-WAN, MPLS and circuit delivery) adds a carrier and the customer's local site team to the picture. The DPM coordinates Orange Business, the carrier, and the customer through circuit ordering, survey, installation, router install and cutover.

Two things make WAN different from LAN: much of the timeline depends on the **carrier** (survey and circuit-installation dates), and the **customer's local team** must actively support — validating scope, granting site access, completing in-house wiring, and escorting engineers. Keep both moving and the plan stays on track.

Source project plan: *WAN Project Timeline*. The Gantt below shows the indicative sequence and duration of each phase.

Project timeline — Gantt chart

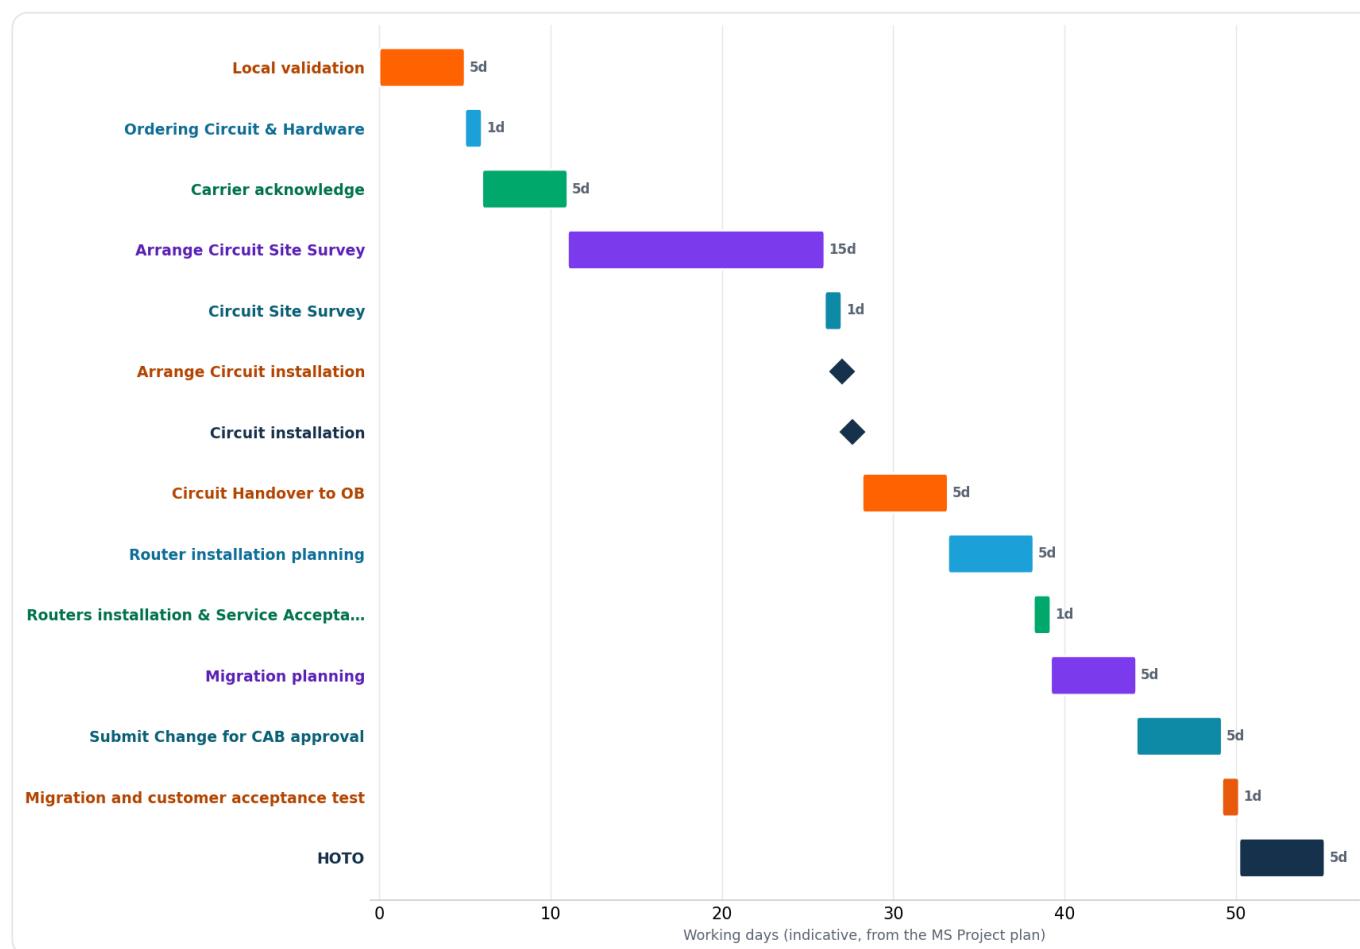

Colour-coded phase timeline for WAN delivery (◆ = milestone). Each bar matches its step card below.

1 Local validation

5d · 2026-08-03 → 2026-08-07

- OB local team will contact Customer local team to validate the order scope, site details, circuit DMARC points, etc
- Customer local team will need to respond to validation request and provide all details as this a mandatory action for OB delivery team to place the order with Carrier.

2 Ordering Circuit & Hardware

1d · 2026-08-03 → 2026-08-03

- 1 Once order validated by Customer local contact, OB delivery team will order the Hardware & Circuit

3 Carrier acknowledge

5d · 2026-08-03 → 2026-08-07

- 1 After placing order with carrier within 2 to 5 days carrier should acknowledge the order.

4 Arrange Circuit Site Survey

15d · 2026-08-03 → 2026-08-21

- 1 Carrier will then contact Customer local team to arrange a site survey in order to confirm the work required to deliver the circuits and the exact delivery dates.
- 2 Customer local team will need to respond back to carrier to confirm a date

5 Circuit Site Survey

1d · 2026-08-03 → 2026-08-03

- 1 Carrier engineer will be on site to run the site survey
- 2 Customer local team will need to grant carrier engineer access to site to complete the site survey.

6 Arrange Circuit installation

Milestone

- 1 "Carrier will contact Customer local team again to arrange the circuit installation activities and install the carrier NTU devices.
- 2 In some cases circuit installation will require landlord approvals which will require Customer local team support and might require multiple visits based on the survey results
- 3 OB expect Customer local team to respond back to carrier and grant them access to complete the circuit installation
- 4 OB expect Customer local team to complete the in-house wiring required to extend the circuit from carrier DMRAC up to the server room where OB routers will be installed

7 Circuit installation

Milestone

- 1 Carrier engineer will be on site to run the circuits installation
- 2 OB expect Customer local team to escort carrier engineer

8 Circuit Handover to OB

5d · 2026-08-03 → 2026-08-07

- 1 After circuit is successfully installed by local carrier, circuit will be handed over to OB team.

9 Router installation planning

5d · 2026-08-03 → 2026-08-07

- 1 Once circuit is handed over, OB Local delivery team will contact Customer local team to arrange the OB routers shipment to Customer
- 2 site & agree on the installation date - In some cases OB engineer can carry the routers with him on the installation date but the standard process is the hardware's should be shipped to site prior to the installation date.
- 3 OB expect Customer local team to confirm the installation date and share the local contact details that will escort OB engineer
- 4 Hardware Shipment to CC site
- 5 Courier will contact Customer local team to ship the new hardware to site.
- 6 Customer local team will need to respond to Courier and collect the new devices.
- 7 Customer local team will need to store the hardware till the installation date and then hand them over to OB engineer.

10 Routers installation & Service Acceptance test

1d · 2026-08-03 → 2026-08-03

- 1 OB engineer will visit Customer site and rack & connect the routers to the WAN connection, OB installation team will remotely support OB engineer and test the connectivity-- LAN connection will be kept unshut at this stage.
- 2 Customer local team are required to escort OB engineer and guide him to the server room where the the devices will be installed.

11 Migration planning

5d · 2026-08-03 → 2026-08-07

- 1 OB & Customer project team will plan a date to cut over the current service and migrate to SD-WAN new solution.
- 2 Customer local & project team will need to confirm a date & down time to activate the LAN connectivity & SD-WAN solution.
- 3 Customer local testers should be available during this agreed window to run the acceptance testing's.
- 4 OB PM will send a team meeting invite for the activity a week in advance to secure all resources.

12 Submit Change for CAB approval

5d · 2026-08-03 → 2026-08-07

- 1 Customer PM will submit a CAB request to be approved prior to the cutover date.

13 Migration and customer acceptance test


1d · 2026-08-03 → 2026-08-03

- 1 OB PM will open the Teams meeting
- 2 OB engineer or Customer local engineer will connect the LAN cables to new routers.
- 3 OB TM team will activate the LAN & test service remotely
- 4 Customer local testers will run the acceptance testing's and confirm service working as expected.

- 1 OB project team will hand over the new site to operation after 7 calendar days from the migration date.
- 2 Customer local & Project team to approve site to exist hyper care & hand over to operation

WAN Delivery — the complete plan, task by task

The complete plan at a glance — every task in order, colour-coded by phase, with its duration from the MS Project plan. Diamonds are milestones.

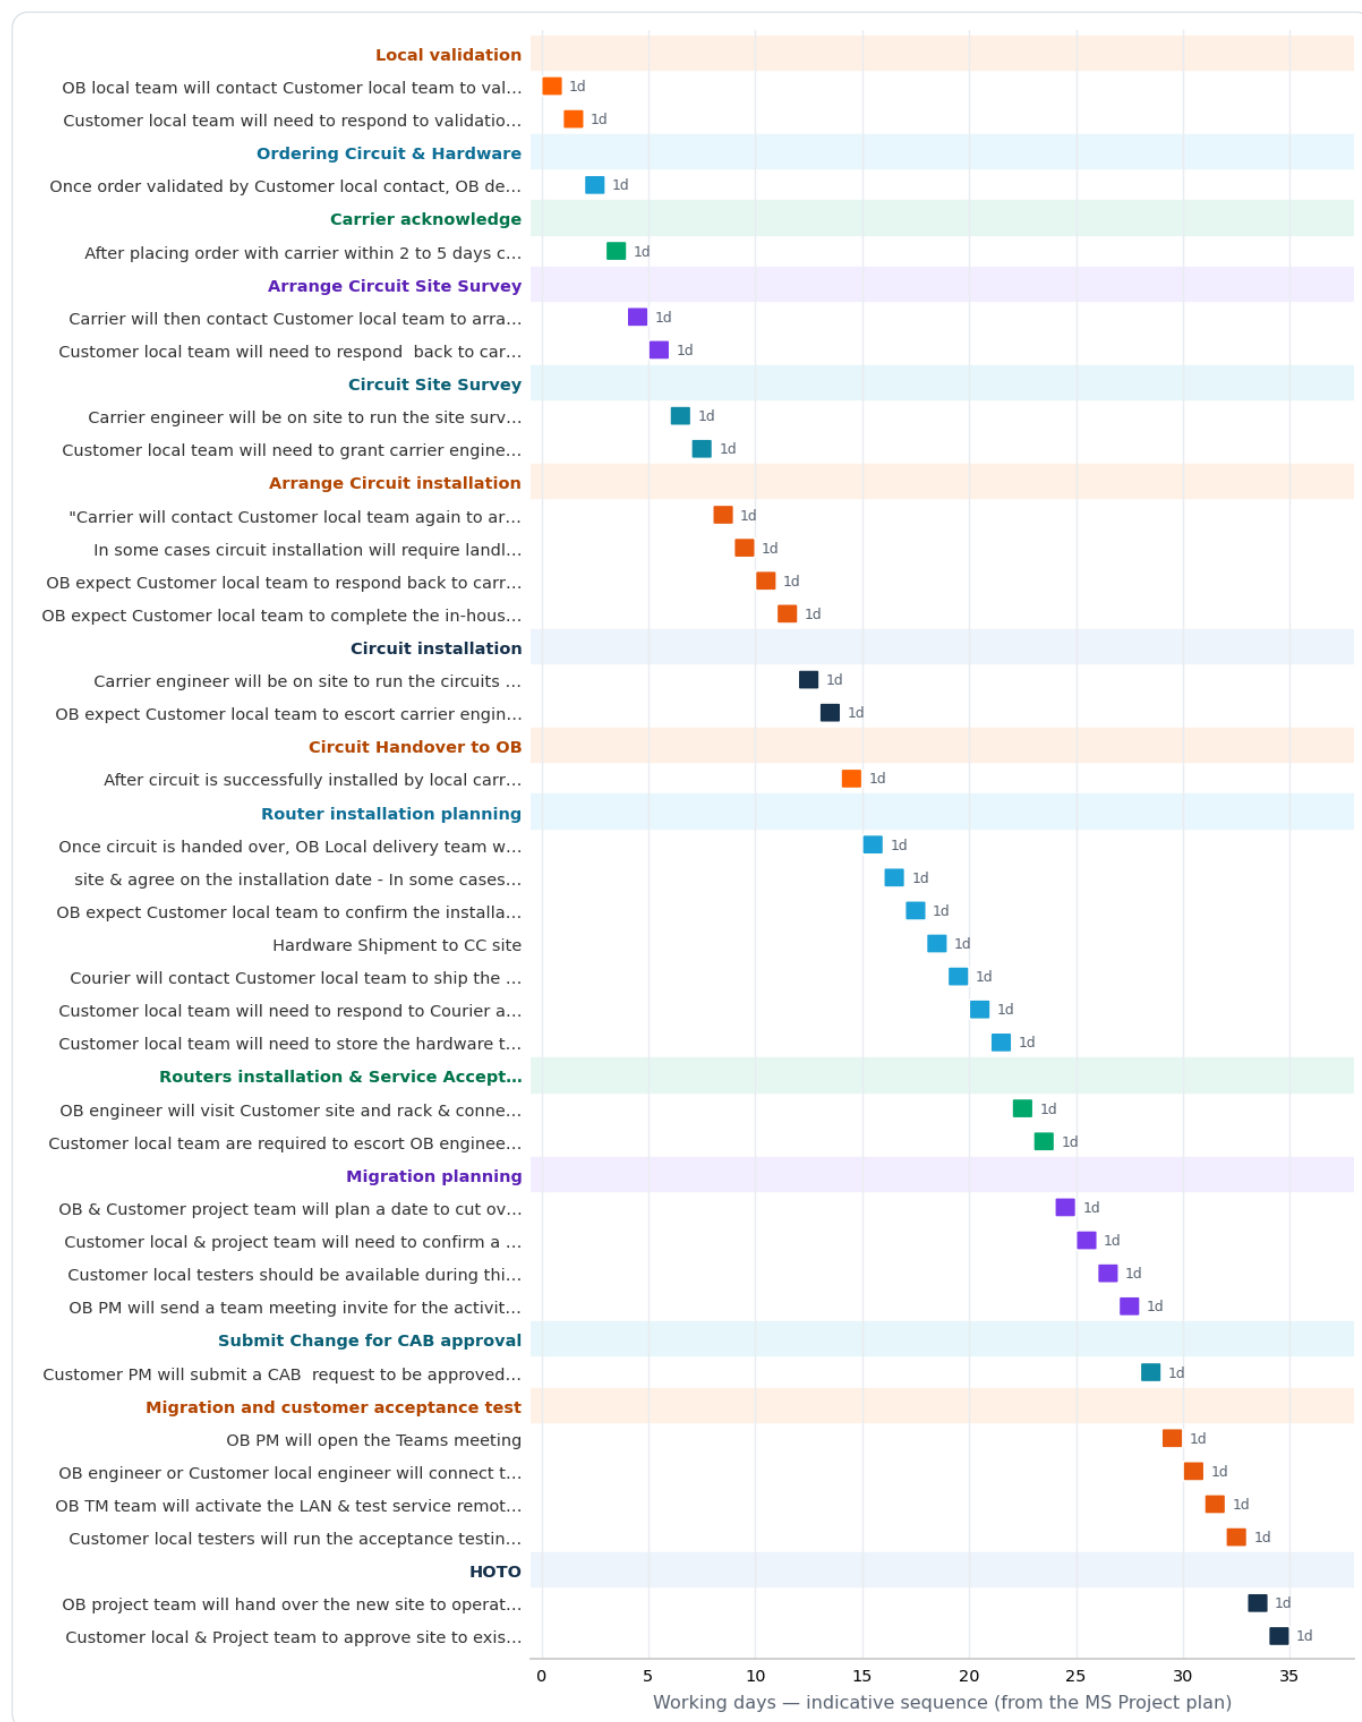

SECTION 8

Networking Fundamentals

You don't need to be a network engineer, but understanding the basics makes every conversation easier. Here's the quick orientation — the Knowledge Base covers each in depth.

TOPIC	THE ONE-LINE IDEA
LAN & WAN	A LAN is the local network at a site; a WAN connects sites together over distance. Most of our work touches both.
IP Routing	How traffic finds its way between networks — addresses, subnets, and protocols like OSPF and BGP.
Switching	Moving traffic within a site — VLANs separate networks, STP prevents loops, trunks carry many VLANs.
Wireless	Access points broadcast Wi-Fi; a controller (WLC) manages them; SSIDs are the network names users see.
Firewalls	Control what traffic is allowed between zones; modern "next-gen" firewalls also inspect applications and threats.
Zscaler	Cloud-delivered security (ZIA/ZPA) built on Zero-Trust and SASE principles — security without backhauling traffic.

SECTION 9

Vendor Hardware

Three vendors come up most often. You'll learn the specific models as you meet them on customer sites.

VENDOR	WHAT THEY MAKE	YOU'LL MEET
Cisco	The broadest portfolio — switching, routing, security and wireless.	Catalyst switches, WLCs, Catalyst APs, ASA/FTD firewalls, Catalyst Center
Palo Alto	Security specialist — next-generation firewalls and cloud security.	PA-Series firewalls, Panorama, Prisma, GlobalProtect
Fortinet	An integrated "Security Fabric" where the firewall manages the whole stack.	FortiGate, FortiSwitch, FortiAP, FortiManager

Want the detail? The Knowledge Base "Devices" hub has a full guide per vendor — port diagrams, model specs and a side-by-side comparison of how each names the same building blocks.

SECTION 10

Your First Few Weeks

A simple path to getting productive. Tick these off with your manager and buddy.

Week 1 — Orient

- ☐ Read this handbook end-to-end and browse the Knowledge Base.
- ☐ Meet your manager and find out which cluster and customers you'll support.
- ☐ Get your accounts and access requested (GOLD, ServiceNow, SharePoint, PRIME).
- ☐ Learn who your SMEs are and how to reach them.

Weeks 2–3 — Shadow

- ☐ Shadow an experienced DPM through a live delivery — sit in on staging and dry-run calls.
- ☐ Follow one project through the phases using the LAN/WAN step lists in Sections 6–7.
- ☐ Watch how MACHX raises and FLIP bookings are made.
- ☐ Start logging your time in Oracle PRIME.

Weeks 4+ — Contribute

- ☐ Take ownership of a small delivery (or a workstream within a larger one) with support.
- ☐ Run a UAT session and prepare a HOTO pack for SharePoint.
- ☐ Pick a squad to join and make your first contribution.

SECTION 11

Key Terms & Where to Get Help

A handful of acronyms you'll hear in your first week. The full, searchable glossary is on the Knowledge Base.

TERM	MEANING
DPM	Delivery Project Manager — you.
HOTO	Hand-Over-To-Operations — the final sign-off handing the delivered environment to support.
VPO / TIM	The engineering/staging resource that performs technical work, requested via MACHX.
SC	Solution Consultant — the technical design owner who joins dry runs.
UAT	User Acceptance Testing — the customer confirms services work after migration.
LLD	Low-Level Design — the detailed technical design document for the build.
CAB	Change Advisory Board — approves the change before a cutover (esp. WAN).
DMARC	The demarcation point — where the carrier's circuit responsibility ends and the customer's begins.
EDD	Estimated Date of Delivery — when ordered hardware is expected.
Option 43	The DHCP setting that tells an AP where to find its controller.

Where to get help

- **Your manager** — your first stop for anything about your deliveries, priorities or access.
- **Your cluster SMEs** — for technical and process questions; find them on your cluster page.
- **The Knowledge Base** — for the process flowcharts, tool references, vendor guides, team directory and glossary.
- **Your buddy / fellow DPMs** — no question is too small in your first weeks.

Welcome aboard. Nobody expects you to know everything on day one. Ask questions, shadow generously, and lean on the team and the Knowledge Base. You'll be running your own deliveries before long.



Orange **Business**

YOU'RE READY

Welcome aboard.

Keep this handbook close, lean on your manager, your SMEs and your fellow DPMS — and use the Network Knowledge Base as your live companion for processes, tools, the team directory and the glossary.
